


| Stations | No | Dist |
|----------|----|------|
| +84      | 14 | ft   |

Section No 12

| Cubic Yards     |           |
|-----------------|-----------|
| Exc             | Emb       |
| 24642.88        | 23.244.36 |
| 290.11          |           |
| 24932.99        | 23.244.36 |
| add side tracks |           |
| 1347.74         |           |
| Total Amt       |           |
| 24.592.13       |           |

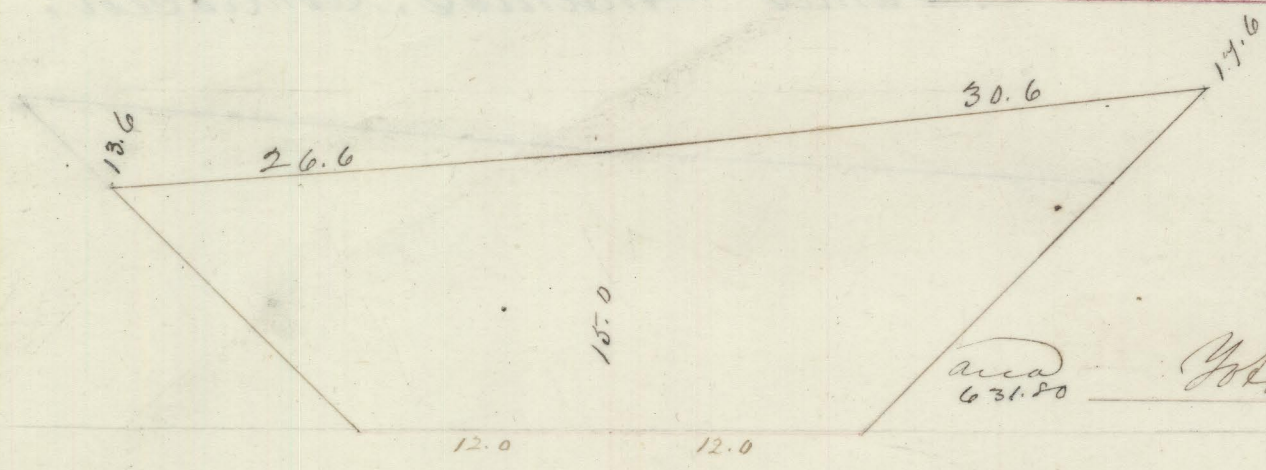

Amt Borrowed

Final Quantities

Grading:-

|   |                       |                       |
|---|-----------------------|-----------------------|
| Total Amt. as exhibited in cross-sections | 24.933 C. Yds. of Ex. | 23.244 C. Yds. Emb.   |
| Add for slides outside of do.             | 100 " " " "           | 485 " " " "           |
| " " Grading for side track near Cresson   | -----                 | 1.348 " " " "         |
| " " Raising Turupike to level of R. R.    | -----                 | 1.068 " " " "         |
| Total amount                              | <u>25.033</u> " " " " | <u>26.145</u> " " " " |
| Amt. of Emb. made from roadway Ex.        | -----                 | <u>25.077</u> " " " " |
| " " do. " " Borrowed materials            | -----                 | <u>1.068</u> " " " "  |

Masonry:-

- 59 Peches in rectangular drains
- 26 " " Paving foundations of do.

Extra work:-

- Extra grubbing & clearing Estimated \$100.→
- Breaking stone on Turupike " \$200.
